https://github.com/Et1enneee/comp3500-logistics

COMP 3500SEF · Final Report

Warehouse Logistics Management System
Group 42: Tang Yi Jie, Yin Pei Xu, Tang Chao, Yang Ting Zhang, Wu Peng Bo, Chung Ngon Man, Li Mu Qiu.

1. Scope

The goals are traceable order decisions and a role-separated workflow. Customers order and track; staff confirm, pick, ship and assign; drivers simulate assigned deliveries; administrators report. The local application serves one warehouse using Next.js, TypeScript, Prisma and SQLite. Real GPS, barcode scanning, recipient telephone collection, payment and carrier integration are outside scope. Operational constraints address deployment and data integrity. Requirements and models link to evidence; §10 collects the trail.

2. Development process

Plan-driven increments have triggers and verified outcomes; integration and continuous integration provide feedback. Product or specification changes form increments; evidence production belongs to hardening. Records establish development, not external delivery.

Table A. Increment, trigger and outcome

Increment and date	Trigger	Outcome
Planning, 9 and 11 Oct 2026	Project selection	Responsibilities and contracts recorded
Test-led review, 17 Oct 2026	Assess order and stock functions	Defects recorded; drove confirmation
Confirmation, 26–28 Oct 2026	Failed endpoint and missing ledger	Transaction verified
Integrated application, 1 Nov 2026	Integrate foundation	Customer, staff and admin workflows
Driver and privacy, 2 Nov 2026	Delivery and data minimisation	Assigned tasks and privacy checks
Documentation hardening, 10–11 Nov 2026	Model and evidence review	Diagrams and traceability aligned
Export simplification, 11 Nov 2026	Scripted walkthrough finding (issue #15)	Selected-date export in three actions; regression passed

The workflow, issue tracker and increment register record integration, problems and context.

3. Requirements

The specification defines obligations and rationale.

Functional requirements and verification

FR	The system shall	Rationale	Verification
FR-01	create orders with product lines and totals	start fulfilment	Test
FR-02	enforce lifecycle and stock reservation or release	protect invariants	Test
FR-03	number orders and shipments and show owner tracking	retrieve progress	Test
FR-04	show inventory, replenishment, ledger and low-stock alerts	support replenishment	Test
FR-05	record event notifications and allow reading	communicate progress	Test
FR-06	provide admin aggregates and CSV export	support review	Test
FR-07	authenticate and enforce role and object access	protect data	Test
FR-08	assign shipped orders and simulate delivery	complete handoff	Test

Non-functional requirements cover NFR-01 performance; NFR-02 integration-point availability; NFR-03 least privilege; NFR-04 scripted operation effort; NFR-05 process quality.

Table B. Risk coverage (detailed mapping)

Risk	Addressed by	Treatment status
RK-01	Increment register	Managed — scheduling plan
RK-02	FR-02, NFR-05	Mitigated — transition tests
RK-03	Priority register	Managed — scope priorities
RK-04	NFR-05	Managed — CI workflow
RK-05	FR-01/04/06, NFR-05	Managed — seed regression test
RK-06	Risk plan	Managed — assessment schedule
RK-07	NFR-05 support	Managed — setup guide
RK-08	Risk plan	Managed — report and video plan

Mitigated records a mitigation; managed records a mechanism while the historical register remains open.

4. System models

Five views link roles, lifecycle, data, transaction, layers. Local transactions preserve consistency without splitting services; state and stock guards enforce rules.

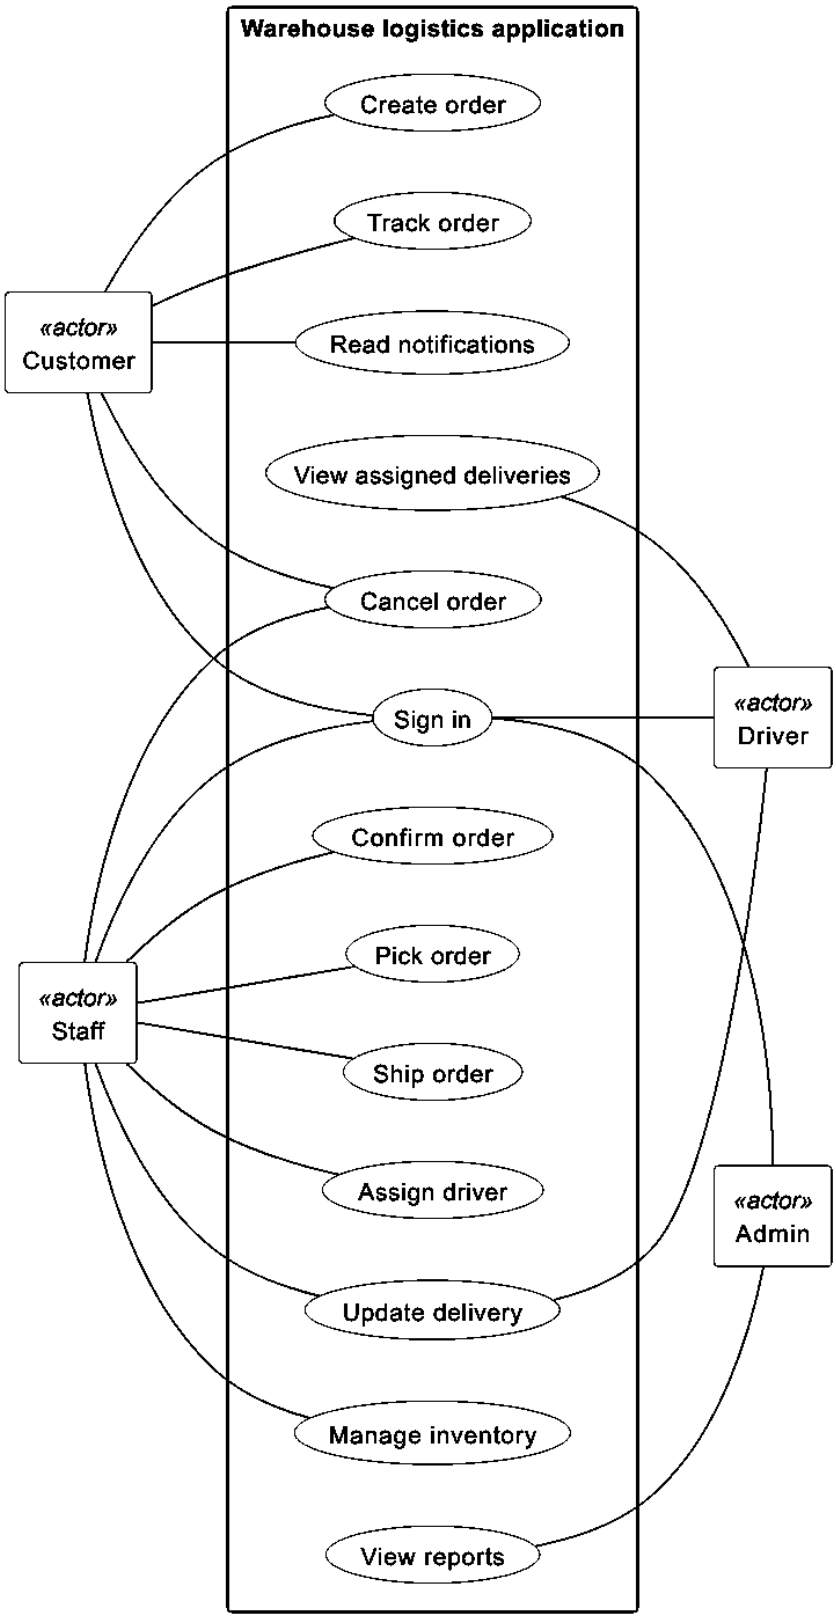


Figure 1. Which roles perform each function? Rebuilt from the reviewed draft; §9. Source.

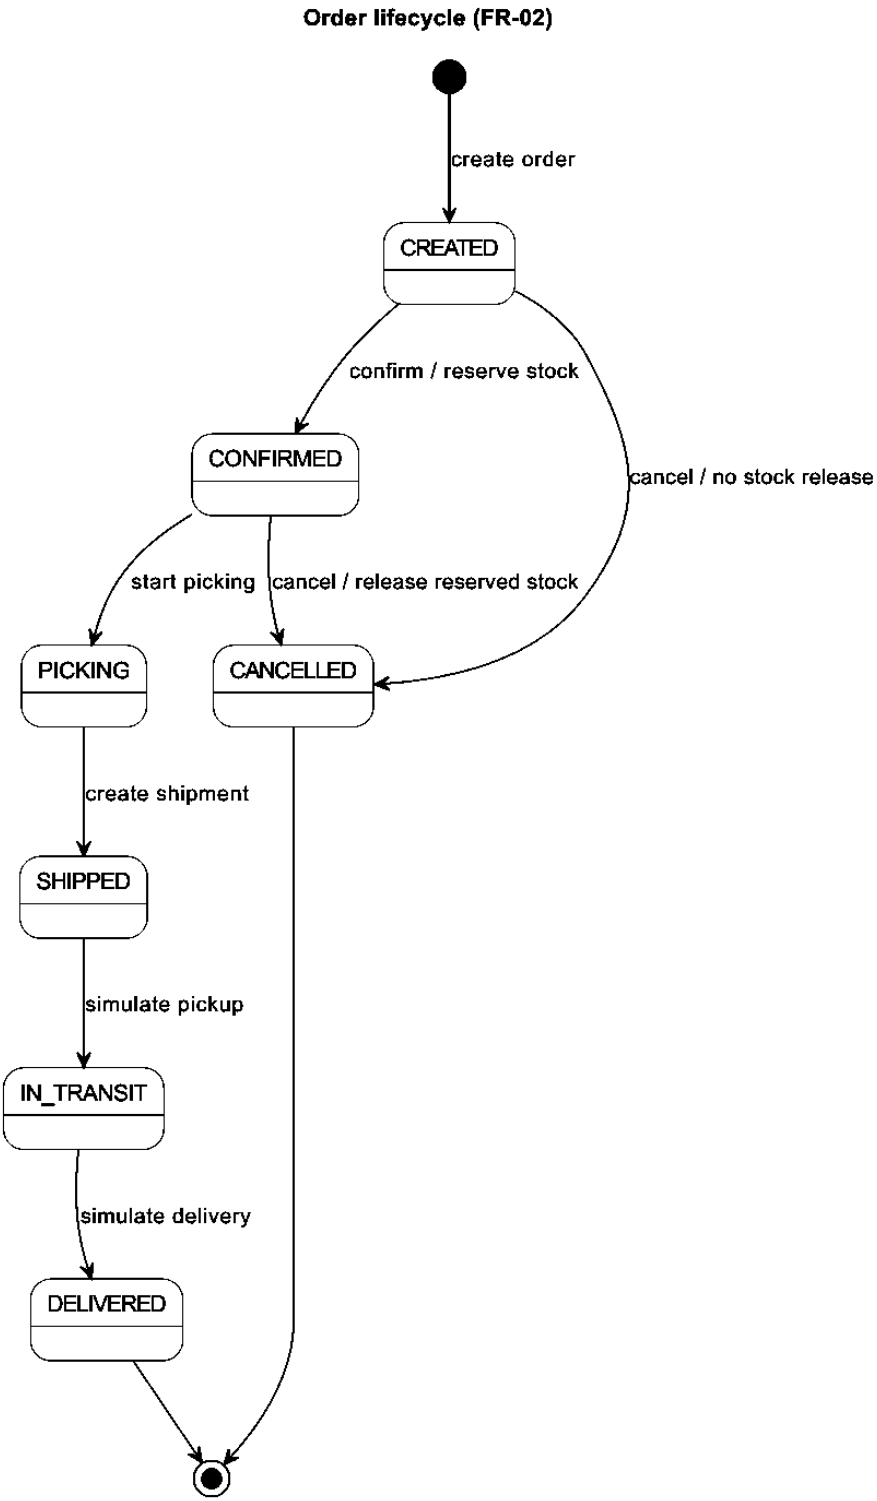


Figure 2. Which order transitions and stock effects are valid? Source.

Each item references one product; each order has 0..1 shipment; each product has 0..* inventory logs.

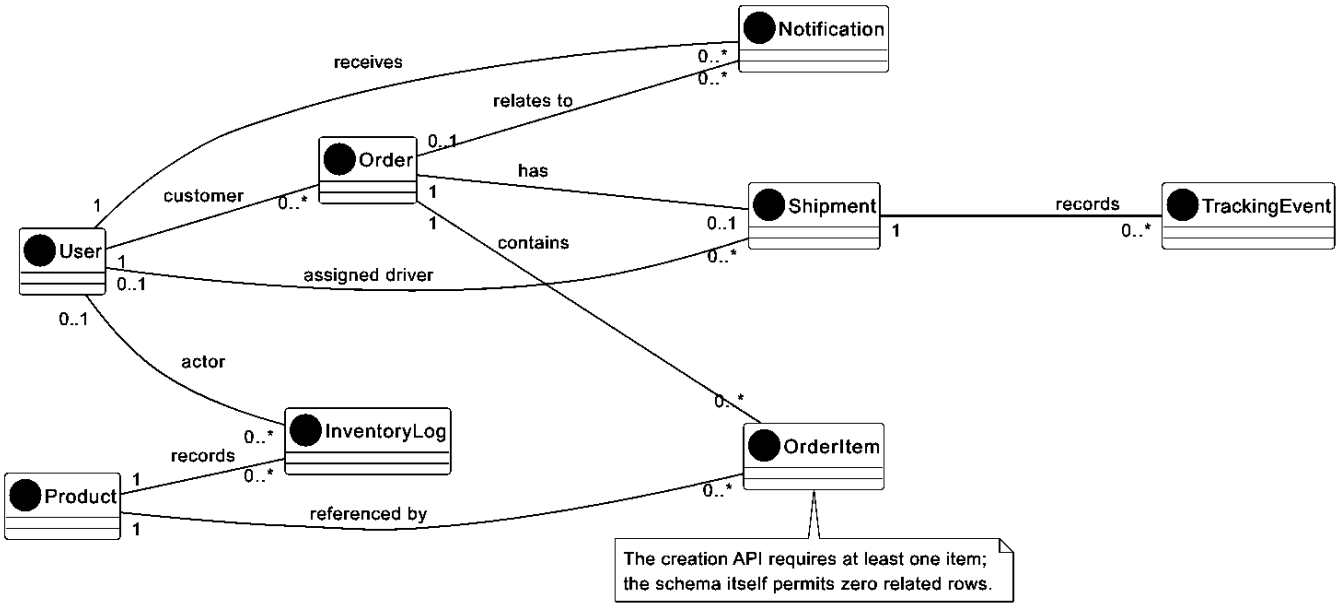


Figure 3. Data relationships: the schema permits zero items; the creation API requires at least one. Source.

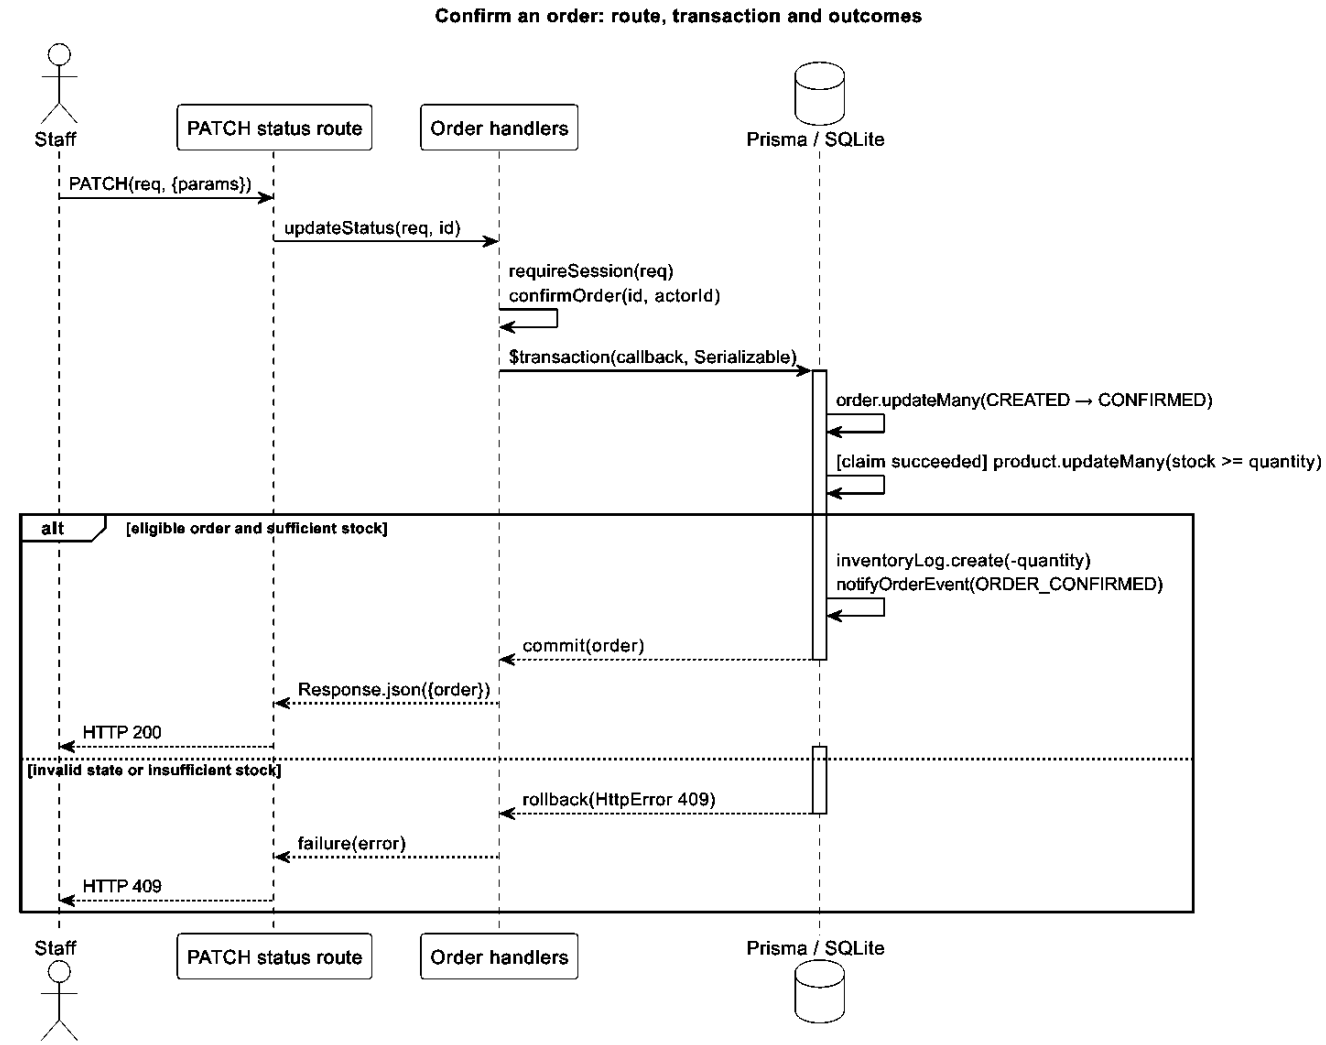


Figure 4. How does confirmation commit or roll back? Source.

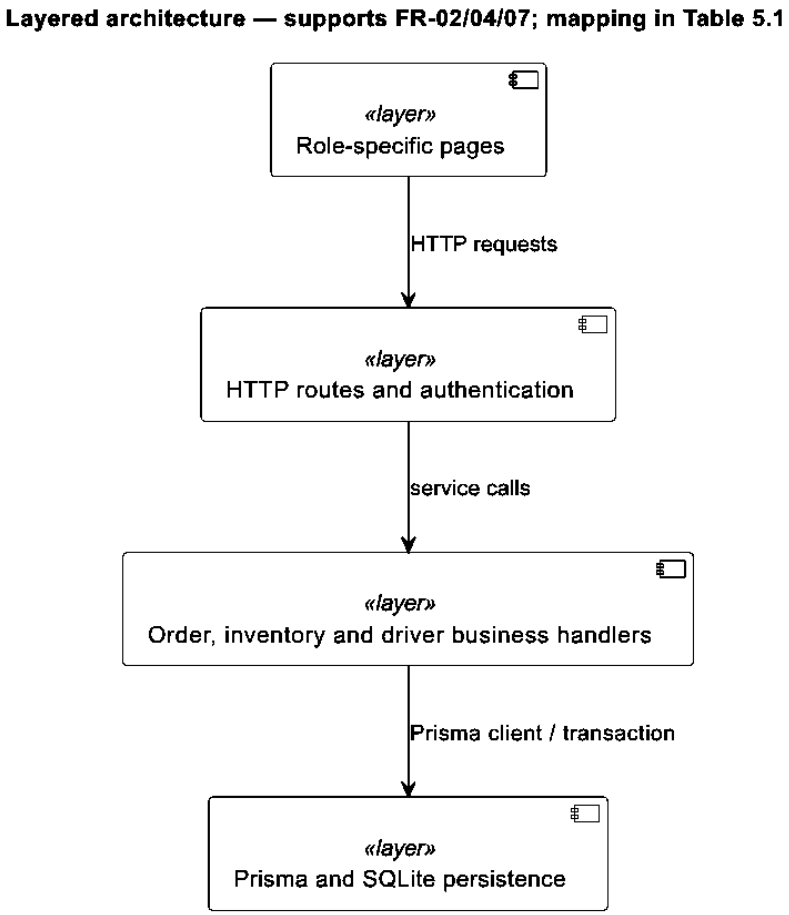


Figure 5. How do four layers connect? Source.

5. Implementation

Design rules map to implementation and tests; staff cancellation requires CONFIRMED.

Design	Implementation	Verification
Guards: CREATED and sufficient stock	order-api.ts:250–253, 276–280	Orders
Serializable state, stock, ledger and notification writes	order-api.ts:245–293	Orders
driverId: assign only SHIPPED; retained after delivery	driver-api.ts:44–51; transition	Driver
Selected-date export	admin/page.tsx:24–48	Browser

6. Verification and validation

Verification checks requirements; validation assesses fitness for users. The regression log and CI show 38 unit, 140 integration, 2 delivery and 26 browser checks.

Boundary case	Observed	Test
Repeat confirmation	HTTP 409; state and stock unchanged	Orders
Stock equals demand	Confirmation succeeds; stock becomes zero	Orders
Stock 4 versus threshold 5	Alert; stock 5 is not low	Inventory

Insufficient stock returns HTTP 409 with unchanged state and stock. In a pre-export-fix local-loopback measurement, API p95 was 3.2–13.6 ms and first-contentful-paint p95 was 64–96 ms, against NFR-01 targets of at most 2 s and 3 s respectively. NFR-02 records 40 successful build–test–browser integration points (observations).

7. Evolution

The early defect record drove the confirmation transaction and retest; the post-presentation audit corrected models and renewed tests. A four-action administrator task became three actions including date entry, or one click from a prepared screen (regression).

8. Validation

The automated walkthrough counts at most three scripted actions across eleven selected operations from prepared screens (excluding login, navigation and recovery). The human protocol defines role tasks, completion, errors, help requests and time, with acceptance criteria defined before each run. Participant observations will be added under this protocol.

9. Feedback and reconciliation

Table C. Feedback to evidence

Feedback	Disposition	Evidence
Diagrams	Corrected models and top-down architecture	Compliance matrix
FR-04	Stock transition effects belong to FR-02	Traceability
Increments	Triggers and outcomes	Register
Presentation p95	Evidence governs; the presentation figure has no tracked measurement in any baseline	Measurement
Admin task	Export re-tested; participant observation planned (§8)	Issue #15
Unit count	Two soak-summary tests increased unit count from 36 to 38	Test history
NFR scope	Criteria revised for local deployment	SRS revision log

Both goals connect order decisions and role-separated workflows to evidence.

10. Evidence

Traceability · Specification · Evidence directory · Baseline record.

Full evidence trail: docs/final-report.md in the repository (evidence baseline `6eb01afb1798c7361205b10597d80c0c26e8fdf6`).
